The Plunge Rehabilitation Project

January 23, 2025 | 07:46:36

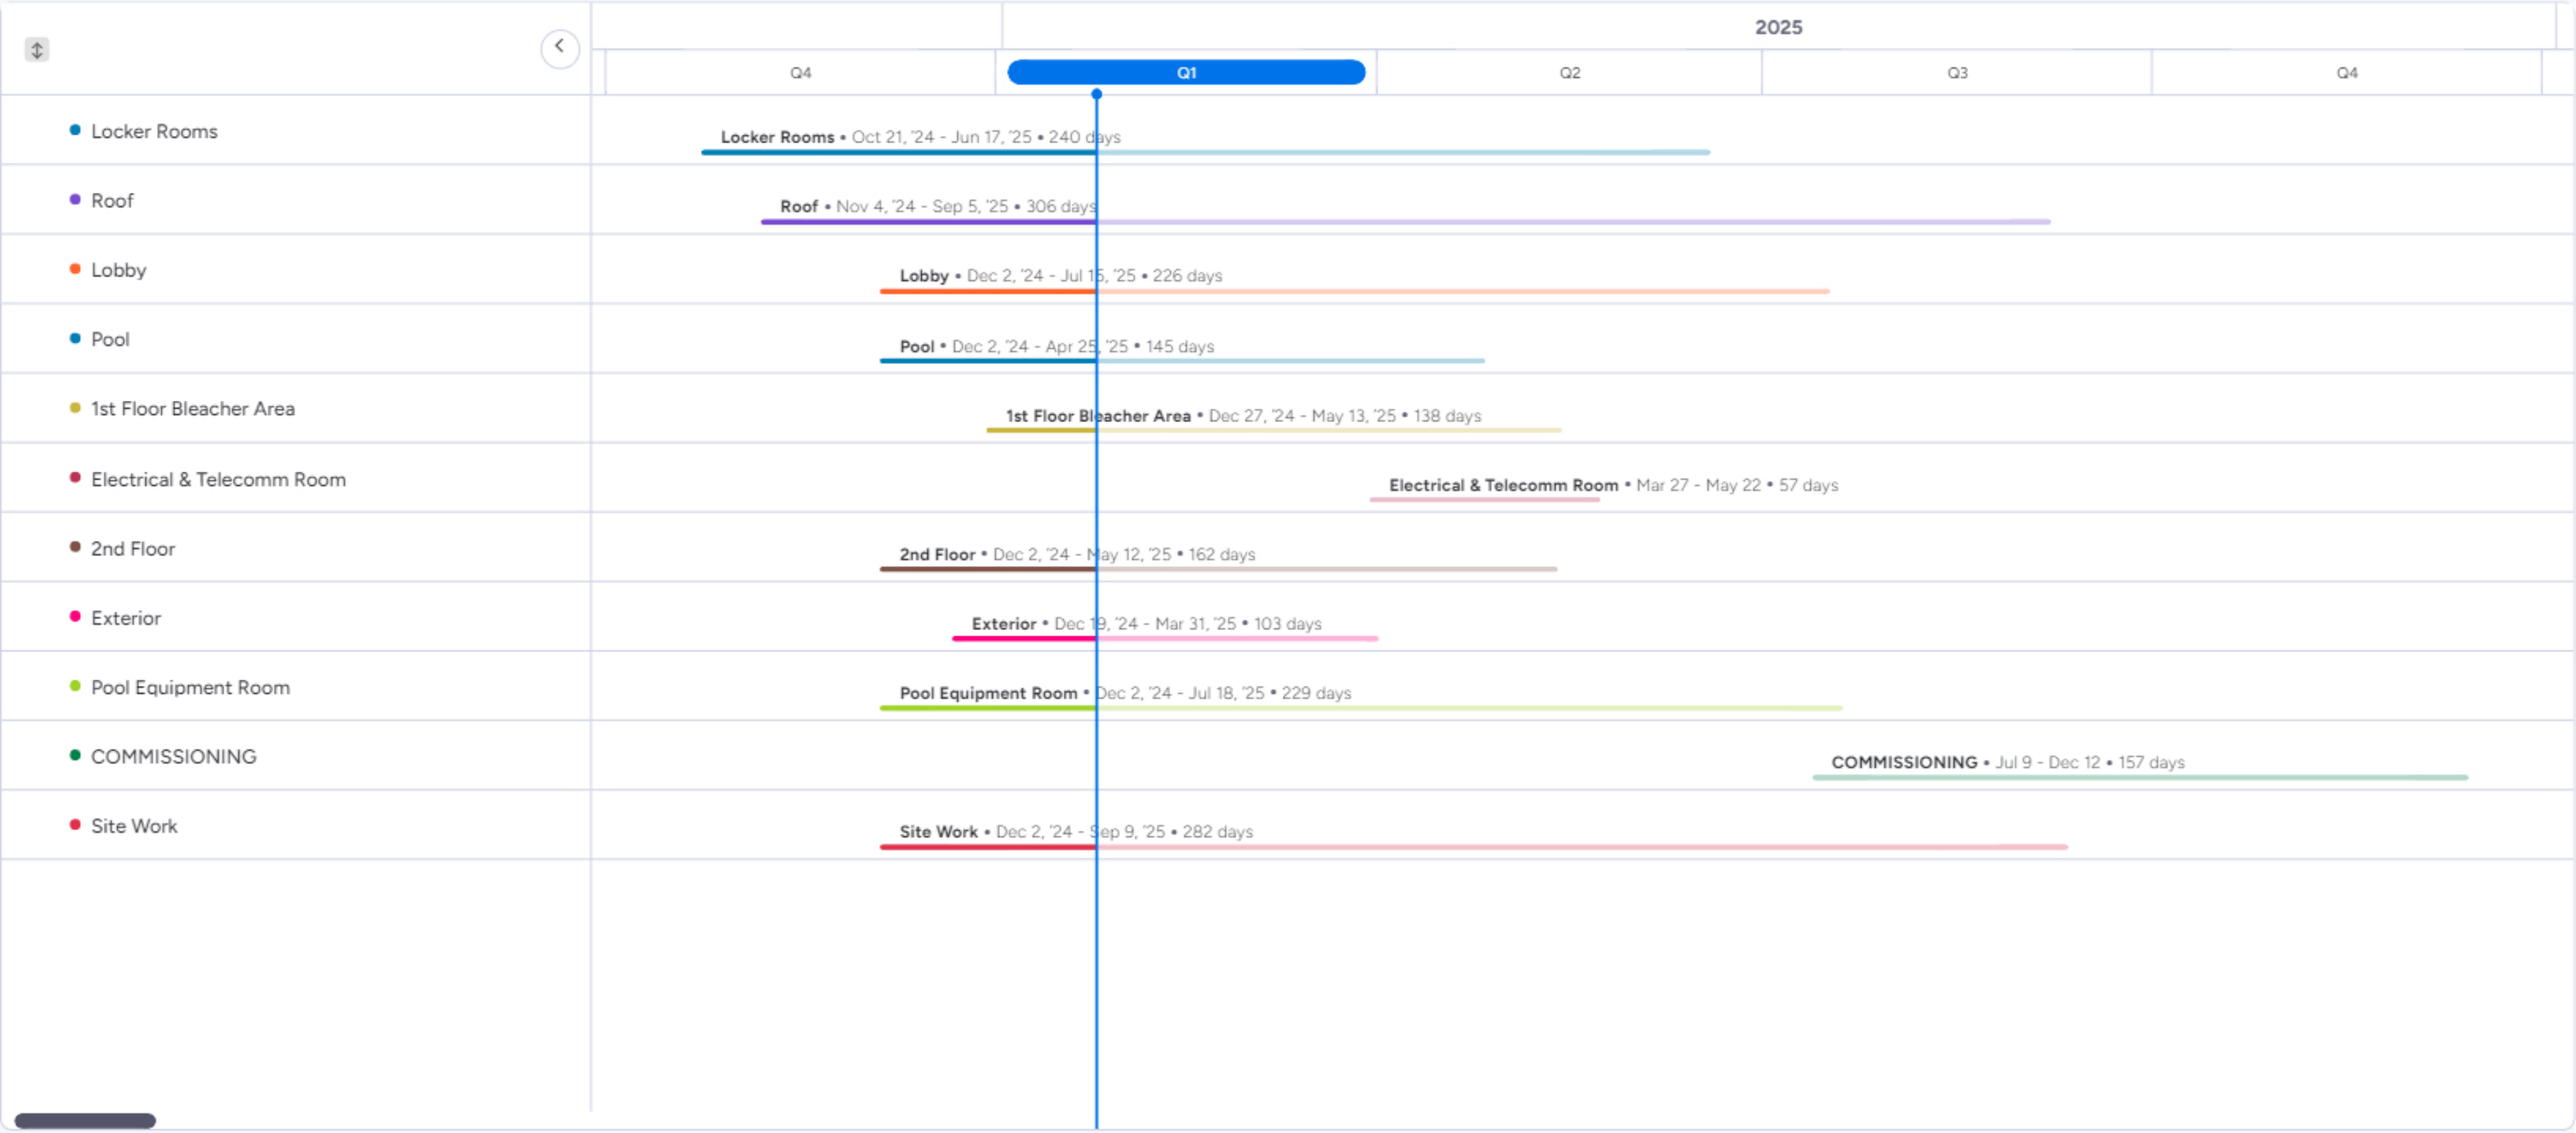

Powered by **monday.com**

Urho Saari Swim Stadium / Plunge Renovation Project

Change Order Log

CO#	Description	Amount	Date Received	Date Responded	Response
1	Switchgear Manufacturer Change - Square D to Eaton	$ -	7/16/2024		
1R1	Switchgear Manufacturer Change - Square D to Eaton	$ 95,697.50	8/27/2024	9/4/2024	Approved.
2	Domestic Water Line Material Change	$ -			
2R1	Domestic Water Line Material Change	$ 5,873.15	8/27/2024	9/25/2024	Approved.
3	New Sensored Flush Valves	$ -	8/23/2024		
3R1	New Sensored Flush Valves	$ 4,554.48	8/27/2024	10/1/2024	Approved.
4	New Anchor Bolts on Terrace per RFI 026	$ 9,280.03	9/16/2024	10/23/2024	Approved.
5	Additional Asbestos Abatement in Locker Room	$ 5,967.99	9/16/2024	10/23/2024	Approved.
6	Edge Metal at Viewing Terrace	$ 3,492.00	9/26/2024	10/23/2024	Approved.
7	Demolish/repair pool wall for main drain	$ 18,928.47	10/25/2024		pending
8	Structural Spall Repair	$ 29,559.05	10/25/2024		pending
8R1	Additional Spall Repair (estimate)	$ 23,000.00			pending
9	Paraflight lifeguard chairs	$ 19,520.71	10/25/2024		pending
10	Removal of self adhered waterproofing	$ (4,800.00)	10/31/2024		pending
11	Hydrojetting of existing roof drains and storm drains.	$ 2,651.29	11/5/2024		pending
12	Replace sewer lines in both locker rooms.	$ 17,506.62	11/6/2024	12/11/2024	Approved.
13	Door hardware change	$ 11,079.97	11/14/2024		pending
14	SCE work not in contract	$ 238,247.37	11/20/2024		pending
15	Conflict between sewer pipe and grade beam	$ 22,372.41	11/20/2024		pending
16	Added tile at 2 drinking fountains	$ 5,235.48	12/20/2024		pending
17	Edge of ramp detail at lowered slab	$ 3,764.07	12/20/2024		pending
18	Existing condition at locker room ramps	$ 7,086.58	12/20/2024		pending
19	ASI 010 - New added footing at existing rear column	$ 7,237.29	12/20/2024		pending
20	Changes to Insulation rating per RFI 007	$ 1,194.33	12/31/2024		pending
21	RFI 096 - Demo interfering brick structure in way of new foot	$ 3,191.10	12/31/2024		pending
	Subtotal	$ 530,639.89			
	Upcoming Change Orders	Estimated Cost			
	Fiber Connection	unk.			
	Bleacher Replacement	$ 56,000.00			
	Pool Tile Replacement (on bottom of pool)	unk.			
	Subtotal	$ 56,000.00			
	TOTAL	**$ 586,639.89**			

Print on: 1/23/2025 7:59 AM
